

Project Definition — EcoMove Solutions

1. Introduction:

EcoMove Solutions is a company founded by Laura Gómez and two partners, specializing in the sale and installation of electric bicycle-sharing systems for municipalities and university campuses. The project aims to prepare the company for operational launch by coordinating business planning, location identification, contractual agreements, equipment procurement, office infrastructure installation, marketing preparation and the launch of promotional activities.

The project is scheduled to start on Monday, 5 October 2026. The working calendar is Monday to Friday, from 08:00 to 15:00, representing seven working hours per day, with weekends treated as non-working days. All three employees are on holiday in August.

The project team consists of Laura Gómez, Project Manager, at €35 per hour; Marc, Technical Specialist, at €22 per hour; and Clara, Administrative Assistant, at €12 per hour. The project plan comprises 12 work activities followed by a zero-duration operational launch milestone.

The planning exercise covers task sequencing, resource allocation, cost estimation, schedule development, critical path analysis, resource leveling and baseline monitoring. The objective is to establish a coordinated and financially transparent plan that supports the company's transition from initial preparation to operational launch.

2. Project Time Configuration and Task Register

2.1 Project Time Configuration

To ensure consistency with the project definition, the working calendar and employee holidays were configured at the project level in Monday.com.

- **Project working schedule — EcoMove Work Schedule:** Monday to Friday, from 08:00 to 15:00, providing seven working hours per day. Weekends are treated as non-working days.
- **Holiday schedule — EcoMove Off Schedule:** 1 August to 31 August, reflecting the annual holidays of all three employees during August.

The screenshots below show the working schedule and holiday configuration in Monday.com. These settings establish the time constraints used for project planning and scheduling.

Additionally, the group members' display names have been updated to match those used in the original project definition. This ensures consistency between the assignment documentation and the resource names displayed in monday.com, making resource identification and assignment verification easier.

Work Schedules

Individual schedules Team schedules

Define availability and time off for your resources, and assign them to keep workloads clear, visible, and balanced.

 Team

Showing: 3 results

☐	Name	Work schedule	Company time off	Personal time off
☐	 Laura	EcoMove Work Schedule ▾	EcoMove off schedule ▾	Edit PTO 
☐	 Marc	EcoMove Work Schedule ▾	EcoMove off schedule ▾	Edit PTO 
☐	 Clara	EcoMove Work Schedule ▾	EcoMove off schedule ▾	Edit PTO 

Figure 1: Project members display names and associated work and holiday schedules

Profile

Personal info

Schedule

Working status

Notifications

Language & region

Password

Session history

Schedule

Choose dates from the calendar or use "Add PTO" to add your personal time off.

Working days and hours

Monday	Tuesday	Wednesday	Thursday	Friday	Saturday	Sunday
08:00 - 15:00	08:00 - 15:00	08:00 - 15:00	08:00 - 15:00	08:00 - 15:00		

Time off 2026

Name	Dates	Days	Type
Public holiday	Aug 1 - Aug 31	31	Company

+ Add time off

Weekly capacity: 35h

Figure 2: Details of Work and Absence schedules used in Monday.com

2.2 Task Register

The Task Register provides a structured overview of the 13 activities comprising the EcoMove Solutions project. It presents each task's identification code, description, configured duration and predecessor relationships, making the planned work sequence clear and traceable to the original assignment.

The register also reflects the resource-leveling adjustment to Task 2, distinguishing its original four-day duration from its revised five-day duration. To ensure readability and avoid omitting information, the graphical view was captured in three Landscape-oriented screenshots, allowing all columns to be displayed clearly.

.. ▾ All items 13 items

Item		Group	Board	Owner	Status	Duration	Predecessor	Dependent On
☐ 13. Operational launch	+	● Phase 3: Impleme...	EcoMove Solutions - Proje...		Not Started	0	12	12. Launch promotion...
☐ 1. Define business requirements	1	● Phase 1: Planning ...	EcoMove Solutions - Proje...	L	Not Started	3	-	
☐ 5. Contact equipment suppliers	+	● Phase 2: Procure...	EcoMove Solutions - Proje...	M C	Not Started	4	2	2. Prepare business pl...
☐ 8. Hire installation subcontractor	+	● Phase 2: Procure...	EcoMove Solutions - Proje...	L C	Not Started	3	4	4. Sign lease agreem...
☐ 2. Prepare business plan	+	● Phase 1: Planning ...	EcoMove Solutions - Proje...	L	Not Started	5	1	1. Define business req...
☐ 6. Purchase charging stations	+	● Phase 2: Procure...	EcoMove Solutions - Proje...	M C	Not Started	2	5	5. Contact equipmen...
☐ 11. Sign municipal agreements	+	● Phase 3: Impleme...	EcoMove Solutions - Proje...	L C	Not Started	3	9	9. Install office infrast...
☐ 9. Install office infrastructure	+	● Phase 3: Impleme...	EcoMove Solutions - Proje...	M	Not Started	4	6,7	6. Purchase ch... +1
☐ 7. Purchase office equipment	+	● Phase 2: Procure...	EcoMove Solutions - Proje...	M C	Not Started	2	4	4. Sign lease agreem...
☐ 4. Sign lease agreement	+	● Phase 1: Planning ...	EcoMove Solutions - Proje...	L C	Not Started	1	3	3. Identify potential l...
☐ 3. Identify potential locations	+	● Phase 1: Planning ...	EcoMove Solutions - Proje...	L	Not Started	5	2	2. Prepare business pl...
☐ 12. Launch promotional campaign	+	● Phase 3: Impleme...	EcoMove Solutions - Proje...	L +2	Not Started	8	10,11	11. Sign municipi... +1
☐ 10. Develop marketing materials	+	● Phase 3: Impleme...	EcoMove Solutions - Proje...	L +2	Not Started	5	8	8. Hire installation su...

+ Add item

Figure 3: Task Register in Monday.com – part 1

▼ All items

Item		Timeline	Baseline of Timeli...	Difference	Laura h	Marc h	Clara h	Laura Cost	Marc Cost
☐ 13. Operational launch	+	Nov 17	Nov 17	0	0	0	0	0	0
☐ 1. Define business requirements	+	Oct 5 - 7	Oct 5 - 7	0	18	0	0	630	0
☐ 5. Contact equipment suppliers	+	Oct 15 - 20	Oct 15 - 20	0	0	8	2	0	176
☐ 8. Hire installation subcontractor	+	Oct 23 - 27	Oct 23 - 27	0	4	0	4	140	0
☐ 2. Prepare business plan	+	Oct 8 - 14	Oct 8 - 14	0	32	0	0	1,120	0
☐ 6. Purchase charging stations	+	Oct 21 - 22	Oct 21 - 22	0	0	6	2	0	132
☐ 11. Sign municipal agreements	+	Nov 2 - 4	Nov 2 - 4	0	8	0	2	280	0
☐ 9. Install office infrastructure	+	Oct 27 - 30	Oct 27 - 30	0	0	16	0	0	352
☐ 7. Purchase office equipment	+	Oct 23 - 26	Oct 23 - 26	0	0	4	3	0	88
☐ 4. Sign lease agreement	+	Oct 22	Oct 22	0	2	0	1	70	0
☐ 3. Identify potential locations	+	Oct 15 - 21	Oct 15 - 21	0	10	0	0	350	0
☐ 12. Launch promotional campaign	+	Nov 5 - 16	Nov 5 - 16	0	4	20	4	140	440
☐ 10. Develop marketing materials	+	Oct 28 - No...	Oct 28 - No...	0	5	12	10	175	264
+ Add item									

Figure 4: Task Register in Monday.com – part 2

▼ All items

Item	Costs	Laura Cost	Marc Cost	Clara Cost	Total Labor Cost	Fixed Cost	Total Cost	EcoMoveApprov...	Baseline Differen...
☐ 13. Operational launch	+	0	0	0	0	0	0	Nov 17	0
☐ 1. Define business requirements	+	630	0	0	630	0	630	Oct 5 - 7	0
☐ 5. Contact equipment suppliers	+	0	176	24	200	0	200	Oct 15 - 20	0
☐ 8. Hire installation subcontractor	+	140	0	48	188	0	188	Oct 23 - 27	0
☐ 2. Prepare business plan	+	1,120	0	0	1,120	0	1,120	Oct 8 - 14	0
☐ 6. Purchase charging stations	+	0	132	24	156	8,000	8,156	Oct 21 - 22	0
☐ 11. Sign municipal agreements	+	280	0	24	304	0	304	Nov 2 - 4	0
☐ 9. Install office infrastructure	+	0	352	0	352	0	352	Oct 27 - 30	0
☐ 7. Purchase office equipment	+	0	88	36	124	0	124	Oct 23 - 26	0
☐ 4. Sign lease agreement	+	70	0	12	82	0	82	Oct 22	0
☐ 3. Identify potential locations	+	350	0	0	350	0	350	Oct 15 - 21	0
☐ 12. Launch promotional campaign	+	140	440	48	628	4,500	5,128	Nov 5 - 16	0
☐ 10. Develop marketing materials	+	175	264	120	559	0	559	Oct 28 - No...	0
+ Add item									

Figure 5: Task Register in Monday.com – part 3

3. Dependency Structure and Gantt Chart

The Gantt Chart provides a visual representation of the EcoMove Solutions project schedule, showing the planned activities, their dates and the dependencies that determine their execution sequence. The dependency links reflect the predecessor relationships specified in the original assignment, including activities with multiple predecessors.

The critical path is highlighted in red and consists of Tasks 1 → 2 → 3 → 4 → 7 → 9 → 11 → 12 → 13. This sequence runs from defining the business requirements through business planning, location identification, lease signing, office equipment procurement, infrastructure installation, municipal agreements and the promotional campaign, culminating in the operational launch milestone. These activities form the critical sequence governing the planned project completion date.

A landscape-oriented screenshot of the Gantt Chart was included in the final report to maximize the readability of task names, schedule dates, dependency connectors and critical path highlighting. The displayed critical path matches the sequence identified in the project planning analysis.

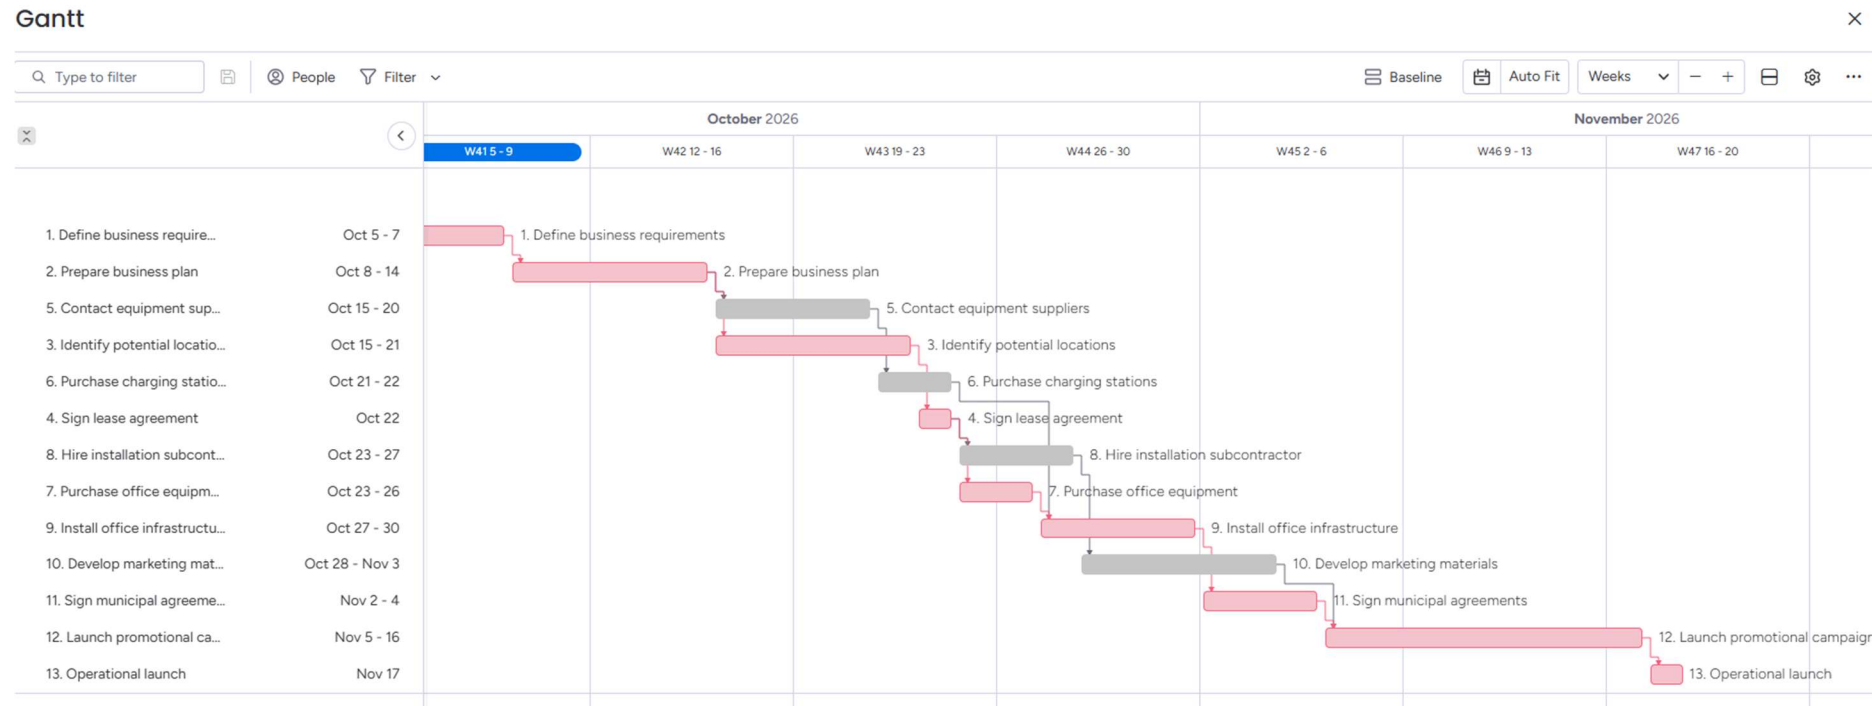


Figure 6: Gantt Chart view showing the tasks precedence and the critical path in red

4. Project Analysis and Key Findings

4.1 Project planning and schedule analysis

The EcoMove Solutions project plan integrates 12 work activities and a final operational launch milestone into a dependency-based schedule. The Gantt Chart identifies the critical path as Tasks 1 → 2 → 3 → 4 → 7 → 9 → 11 → 12 → 13, highlighting the sequence of activities that governs the planned completion date.

Resource leveling required extending Task 2, Prepare business plan, from four to five working days while retaining Laura's 32 assigned hours. This adjustment reduces her average assigned workload on that task from eight to 6.4 hours per working day, bringing it within the specified seven-hour daily capacity. The revised schedule preserves the assigned effort and associated labour cost.

4.2 Budget analysis

The total planned project budget is **€17,193**, comprising €4,693 in labour costs and €12,500 in fixed costs. Labour costs are calculated from the assigned hours and hourly rates of the three team members. The fixed costs comprise €8,000 for charging stations under Task 6 and €4,500 for the promotional campaign under Task 12. This breakdown provides a transparent financial estimate for the planned project activities.

4.3 Key project management challenges

The planning exercise addresses four main challenges:

1. **Schedule coordination:** Managing task dependencies and identifying activities that directly affect the planned completion date.
2. **Resource capacity:** Adjusting task duration to accommodate the team's working-hour constraints while preserving assigned effort.
3. **Cost control:** Combining labour and fixed costs to establish a consistent project budget.
4. **Future monitoring:** Using the approved baseline as a reference for identifying schedule changes and assessing deviations during execution.

5. Resource Planning and Assignments

Resource allocation matrix — assigned effort in hours

Code	Activity	Laura Marc Clara Total			
1	Define business requirements	18	0	0	18
2	Prepare business plan	32	0	0	32
3	Identify potential locations	10	0	0	10
4	Sign lease agreement	2	0	1	3
5	Contact equipment suppliers	0	8	2	10
6	Purchase charging stations	0	6	2	8
7	Purchase office equipment	0	4	3	7
8	Hire installation subcontractor	4	0	4	8
9	Install office infrastructure	0	16	0	16
10	Develop marketing materials	5	12	10	27
11	Sign municipal agreements	8	0	2	10
12	Launch promotional campaign	4	20	4	28
13	Operational launch milestone	0	0	0	0
Total assigned hours		83	66	28	177

The totals reconcile with the original assignment: Laura has 83 assigned hours, Marc has 66 hours and Clara has 28 hours, giving a total of 177 assigned hours.

Resource profiles and hourly rates

Resource	Role	Hourly rate	Assigned hours	Labour cost
Laura Gómez	Project Manager	€35	83	€2,905
Marc	Technical Specialist	€22	66	€1,452
Clara	Administrative Assistant	€12	28	€336
Total			177	€4,693

Labour costs are calculated by multiplying each resource's assigned hours by the corresponding hourly rate. For example, Laura's labour cost is $83 \times €35 = €2,905$. The total planned labour cost is €4,693.

6. Resource Allocation Analysis and Leveling

Resource allocation analysis evaluates the distribution of assigned working hours across the project schedule to identify potential resource overallocations. Resource leveling was applied to Task 2, *Prepare business plan*, extending its duration from four to five working days while retaining Laura's 32 assigned hours. This reduces her average workload on the task from 8 to 6.4 hours per working day, within the specified seven-hour daily capacity, without increasing the planned labour cost. The workload analysis and revised schedule provide a basis for assessing resource capacity and the impact of leveling on the project timeline.

7. Project Duration, Budget and Baseline Monitoring

7.1 Project duration

The EcoMove Solutions project is scheduled to start on 5 October 2026 and reach its operational launch milestone on 17 November 2026, according to the Gantt Chart. The schedule follows the specified Monday-to-Friday working calendar, with seven working hours per day and weekends treated as non-working days.

The critical path consists of Tasks $1 \rightarrow 2 \rightarrow 3 \rightarrow 4 \rightarrow 7 \rightarrow 9 \rightarrow 11 \rightarrow 12 \rightarrow 13$, identifying the sequence of activities that governs the planned operational launch. Resource leveling extended Task 2, *Prepare business plan*, from four to five working days while preserving Laura's 32 assigned hours and keeping her average assigned workload on that task within the seven-hour daily capacity.

7.2 Project budget

The total planned project budget is €17,193, comprising €4,693 in labour costs and €12,500 in fixed costs. Labour costs are calculated from the assigned hours and hourly rates of the three project resources. Fixed costs comprise €8,000 for charging stations under Task 6 and €4,500 for the promotional campaign under Task 12.

This consolidated estimate provides a financial reference for the planned activities and supports cost monitoring during project execution.

7.3 Baseline and future monitoring

The project baseline provides a reference for monitoring the schedule as the project progresses. Comparing current task dates with the approved plan can help identify schedule changes and assess their potential impact on the planned operational launch.

The baseline information configured in Monday.com supports this monitoring process. The baseline representation and any available schedule-variance indicators should be interpreted according to the features actually verified in the project board.

8. Conclusion

The EcoMove Solutions project plan brings together the activities, dependencies, schedule, resource assignments and cost estimates required to prepare the business for operational launch. The Task Register and Gantt Chart provide a structured overview of the planned work, its sequencing and the critical path leading to the operational launch milestone on 17 November 2026.

The resource planning process consolidates 177 assigned working hours across Laura Gómez, Marc and Clara, with a total planned labour cost of €4,693. Resource leveling extended Task 2, *Prepare business plan*, from four to five working days while preserving Laura's assigned hours and reducing her average daily workload on that task to 6.4 hours.

The total planned project budget is €17,193, including €4,693 in labour costs and €12,500 in fixed costs. The project schedule and baseline arrangements provide a foundation for monitoring progress and identifying potential deviations during execution.

Overall, the planning exercise establishes a coordinated approach to project scheduling, resource allocation and cost control, supporting EcoMove Solutions in its preparation for operational launch.
